


# HANDOUT 9A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 38)

## MAY 16, 2018 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2018				2019				2020				2021				2022				2023			
							Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
1	IM Installation (Note that IM3 is currently in operation and will remain in operation until directed otherwise by agencies)	512 days	Thu 1/22/04	Tue 12/20/05	Thu 1/22/04	Tue 12/20/05																								
32	IM3 Cultural Resources Management Plan (IM3 CRMP)	986 days	Thu 7/1/04	Mon 3/10/08	Thu 7/1/04	Mon 3/10/08																								
37	Extraction Well PE-1/Facilities	230 days	Mon 3/21/05	Fri 1/27/06	Mon 3/21/05	Fri 1/27/06																								
47	Supplemental Extraction Well and Facilities	127 days	Fri 7/29/05	Thu 1/19/06	Fri 7/29/05	Thu 1/19/06																								
55	Decommissioning of IM2 Batch Treatment	1182 days	Fri 8/5/05	Fri 1/29/10	Fri 8/5/05	Fri 1/29/10																								
66	Interim Measures and Treated Water Management	751 days	Mon 5/3/04	Fri 2/16/07	Mon 5/3/04	Fri 2/16/07																								
210	Public Participation Plan	578 days	Mon 12/20/04	Fri 2/9/07	Mon 12/20/04	Fri 2/9/07																								
219	Baseline Resources Assessments	897 days	Mon 11/1/04	Mon 3/10/08	Mon 11/1/04	Mon 3/10/08																								
233	Sitewide CEQA Documentation	586 days	Wed 5/17/06	Fri 8/1/08	Wed 5/17/06	Fri 8/1/08																								
237	Programmatic Biological Assessment (PBA)	1920 days	Tue 12/19/06	Tue 4/15/14	Tue 12/19/06	Tue 4/15/14																								
250	REMEDIAL FACILITY INVESTIGATION/REMEDIAL INVESTIGATION (RFI/RI)	6181.25 days	Sat 2/24/96	Tue 9/24/19	Sat 2/24/96	NA																								
251	Historical RFI/RI Reports (Feb. 2005 and Prior Versions)	2455 days	Sat 2/24/96	Fri 7/8/05	Sat 2/24/96	Fri 7/8/05																								
269	Prepare Site History Report (Vol 1)	466 days	Tue 11/15/05	Wed 8/15/07	Tue 11/15/05	Wed 8/15/07																								
284	Prepare RFI/RI Vol 1 Addendum	1829 days	Wed 7/11/07	Tue 7/8/14	Wed 7/11/07	Tue 7/8/14																								
306	Prepare Final Groundwater RFI/RI (Vol 2)	1948 days	Mon 6/27/05	Fri 11/16/12	Mon 6/27/05	Fri 11/16/12																								
616	ADEQ Topock Groundwater Study	475 days	Thu 11/18/04	Wed 8/23/06	Thu 11/18/04	Wed 8/23/06																								
620	Prepare Final Soil RFI/RI (Vol 3)	3454.25 days	Sat 7/15/06	Tue 9/24/19	Sat 7/15/06	NA																								
621	Implementation of Off-site Soil Sampling (Part A Phase 1) and Data Gaps Evaluation	1215 days	Sat 7/15/06	Fri 2/25/11	Sat 7/15/06	Fri 2/25/11																								
770	Draft On-site Soil Sampling (Part B) DQOs	1122 days	Wed 12/6/06	Fri 3/11/11	Wed 12/6/06	Fri 3/11/11																								
825	Soil RFI/RI Work Plan	1211 days	Tue 1/4/11	Mon 8/24/15	Tue 1/4/11	Mon 8/24/15																								
922	Work Plan Implementation/Data Gaps Analysis	594 days	Tue 8/25/15	Thu 11/30/17	Tue 8/25/15	Thu 11/30/17																								
978	Reporting	591.25 days	Tue 6/20/17	Tue 9/24/19	Tue 6/20/17	NA																								
979	Soil Risk Assessment	454.5 days	Tue 6/20/17	Fri 3/15/19	Tue 6/20/17	NA																								
980	Agency Direction to Move Forward with Soil Risk Assessment	1 day	Tue 6/20/17	Tue 6/20/17	Tue 6/20/17	Tue 6/20/17																								
981	Data Summary for EPCs Calculation	5.4 wks	Wed 6/21/17	Fri 7/28/17	Wed 6/21/17	Fri 7/28/17																								
982	Prepare/submit Draft Soil Risk Assessment Report	54 wks	Mon 7/31/17	Fri 8/10/18	Mon 7/31/17	NA																								
983	Calculate Exposure Point Concentrations (EPCs)	4.05 mons	Mon 7/31/17	Fri 11/24/17	Mon 7/31/17	Fri 11/24/17																								
984	Meeting to discuss EPCs	1 day	Wed 8/16/17	Wed 8/16/17	Wed 8/16/17	Wed 8/16/17																								
985	DTSC send Soil Risk Evaluation to CWG/TWG	3 days	Mon 8/13/18	Wed 8/15/18	NA	NA																								
986	DTSC review/comment	46 edays	Thu 8/16/18	Mon 10/1/18	NA	NA																								
987	DOI review/comment	46 edays	Thu 8/16/18	Mon 10/1/18	NA	NA																								
988	CWG/TWG review/comment	32 edays	Thu 8/16/18	Mon 9/17/18	NA	NA																								
989	Tribes review/comment	32 edays	Thu 8/16/18	Mon 9/17/18	NA	NA																								
990	Review/compile Comment Table (duration will be verified after receipt of comments and directives)	2 wks	Tue 10/2/18	Mon 10/15/18	NA	NA																								
991	DTSC/DOI/PG&E hold comment clarification meeting (date is tentative)	0 days	Thu 10/4/18	Thu 10/4/18	NA	NA																								
992	Prepare/send RTC Table (duration will be verified after receipt of comments)	4 wks	Tue 10/16/18	Mon 11/12/18	NA	NA																								
993	RTC Meeting	10 days	Mon 11/19/18	Mon 12/3/18	NA	NA																								
994	Send agenda (2 wks prior to meeting)	0 days	Mon 11/19/18	Mon 11/19/18	NA	NA																								
995	Hold Meeting	0 days	Mon 12/3/18	Mon 12/3/18	NA	NA																								
996	Finalize/submit Final Soil Risk Assessment Report with RTC Table (duration is estimated, to be verified after completion of RTCs)	2.5 mons	Tue 12/4/18	Wed 2/13/19	NA	NA																								
997	DTSC review/approve	1 mon	Thu 2/14/19	Fri 3/15/19	NA	NA																								



Project: PG&E Topock Remediation Project  
 Date: Fri 5/11/18  
 Page 1 of 4

Tasks Not Started/In Progress Overall Task Duration Manual Task Start-only

Tasks Finished Inactive Task Duration-only Finish-only

Baseline Schedule Inactive Milestone Manual Summary Rollup

Milestone Inactive Summary Manual Summary

edays = calendar days; days = work days  
 Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).  
 \*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:  
 PG&E Federal Agencies CWG/TWG Public  
 DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions  
 - Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.  
 - Actual dates may vary depending on field conditions.

# HANDOUT 9A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 38)

## MAY 16, 2018 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2018				2019				2020				2021				2022				2023			
							Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
998	DOI review/approve	1 mon	Thu 2/14/19	Fri 3/15/19	NA	NA																								
999	RFI/RI Volume 3	563.25 days	Fri 7/28/17	Tue 9/24/19	Fri 7/28/17	NA																								
1000	Prepare Draft RFI/RI Vol 3 Report	19.25 mons	Fri 7/28/17	Wed 2/13/19	Fri 7/28/17	NA																								
1001	DTSC sends report to CWG/TWG and Tribes	3 days	Wed 2/13/19	Mon 2/18/19	NA	NA																								
1002	CWG/TWG review/comment	30 edays	Mon 2/18/19	Wed 3/20/19	NA	NA																								
1003	Tribes review/comment	30 edays	Mon 2/18/19	Wed 3/20/19	NA	NA																								
1004	DTSC review/comment	45 edays	Mon 2/18/19	Thu 4/4/19	NA	NA																								
1005	DOI review/comment	45 edays	Mon 2/18/19	Thu 4/4/19	NA	NA																								
1006	Review/compile Comment Table (duration will be verified after receipt of comments and directives)	31 edays	Fri 4/5/19	Mon 5/6/19	NA	NA																								
1007	DTSC/DOI/PG&E hold comment clarification meeting (date is tentative)	0 days	Mon 4/8/19	Mon 4/8/19	NA	NA																								
1008	Prepare/send RTC Table (duration will be verified after receipt of comments)	4 wks	Tue 5/7/19	Tue 6/4/19	NA	NA																								
1009	RTC Meeting	10 days	Tue 6/11/19	Tue 6/25/19	NA	NA																								
1010	Send agenda (2 wks prior to meeting)	0 days	Tue 6/11/19	Tue 6/11/19	NA	NA																								
1011	Hold Meeting	0 days	Tue 6/25/19	Tue 6/25/19	NA	NA																								
1012	Prepare Revised RFI Volume 3 with RTC Table (duration is estimated, to be verified after completion of RTCs)	2 mons	Wed 6/26/19	Fri 8/23/19	NA	NA																								
1013	DTSC review/approve Revised RFI/RI Vol. 3 Report	1 mon	Mon 8/26/19	Tue 9/24/19	NA	NA																								
1014	DOI review/approve Revised RFI/RI Vol. 3 Report	1 mon	Mon 8/26/19	Tue 9/24/19	NA	NA																								
1015	GROUNDWATER CORRECTIVE MEASURES/REMEDIAL ALTERNATIVE DEVELOPMENT	2835 days	Mon 3/29/04	Wed 12/31/14	Mon 3/29/04	Wed 12/31/14																								
1163	CORRECTIVE MEASURE STUDY/FEASIBILITY STUDY (CMS/FS) AND RISK ASSESSMENT	4636.25 days	Mon 12/16/02	Wed 8/12/20	Mon 12/16/02	NA																								
1345	STATEMENT OF BASIS	2882.85 days	Mon 1/4/10	Mon 1/11/21	Mon 1/4/10	NA																								
1360	RECORD OF DECISION	2984 days	Fri 12/18/09	Mon 5/17/21	Fri 12/18/09	NA																								
1383	Section 106 Programmatic Agreement (PA)	1858 days	Fri 10/10/08	Wed 11/18/15	Fri 10/10/08	NA																								
1416	EIR DOCUMENTATION	1449 days	Thu 9/1/05	Wed 3/2/11	Thu 9/1/05	Wed 3/2/11																								
1489	DESIGN, PERMITTING, AND CONSTRUCTION OF GROUNDWATER REMEDY	1889 days	Mon 1/31/11	Tue 4/24/18	Mon 1/31/11	Tue 4/24/18																								
1490	Corrective Measure Implementation/Remedial Design (CMI/RD) Workplan	199 days	Mon 1/31/11	Thu 11/3/11	Mon 1/31/11	Thu 11/3/11																								
1504	Remedial Design (Preliminary, Intermediate, and Pre-Final/Final)	1723 days	Tue 9/20/11	Tue 4/24/18	Tue 9/20/11	Tue 4/24/18																								
1505	Preliminary Design	174 days	Tue 9/20/11	Thu 5/17/12	Tue 9/20/11	Thu 5/17/12																								
1517	Intermediate Design	501 days	Fri 5/18/12	Fri 4/18/14	Fri 5/18/12	Fri 4/18/14																								
1546	Implementation Plan for Evaluation of Alternative Freshwater Sources	422 days	Fri 11/16/12	Mon 6/30/14	Fri 11/16/12	Mon 6/30/14																								
1585	Field Verification of Archaeological/Historical Sites in Groundwater Remedy Footprint	4 days	Tue 9/9/14	Fri 9/12/14	Tue 9/9/14	Fri 9/12/14																								
1586	Prepare/submit Field Verification Report	28 days	Mon 9/15/14	Wed 10/22/14	Mon 9/15/14	Wed 10/22/14																								
1587	Survey of Archaeological/Historical Sites in Expanded Area at Park Moabi	1 day	Tue 12/2/14	Tue 12/2/14	Tue 12/2/14	Tue 12/2/14																								
1588	Survey of Biological Resources in Expanded Area at Park Moabi	3 days	Wed 11/19/14	Fri 11/21/14	Wed 11/19/14	Fri 11/21/14																								
1589	Annual archeological monitoring and site condition assessments	7 days	Thu 12/11/14	Fri 12/19/14	Thu 12/11/14	Fri 12/19/14																								
1590	Pre-Final/Final Design (include plan for decommissioning, removal, and restoration of IM3 facility)	423 days	Mon 4/7/14	Wed 11/18/15	Mon 4/7/14	Wed 11/18/15																								
1639	Construction/Remedial Action Work Plan	423 days	Mon 4/7/14	Wed 11/18/15	Mon 4/7/14	Wed 11/18/15																								
1649	State CEQA Evaluation	793 days	Mon 4/13/15	Tue 4/24/18	Mon 4/13/15	Tue 4/24/18																								
1650	Notice of Preparation	39 days	Mon 4/13/15	Thu 6/4/15	Mon 4/13/15	Thu 6/4/15																								
1651	Scoping Meetings	21 days	Tue 5/12/15	Tue 6/9/15	Tue 5/12/15	Tue 6/9/15																								
1652	Preparation of Draft Subsequent EIR (SEIR)	387 days	Mon 9/7/15	Mon 2/27/17	Mon 9/7/15	Mon 2/27/17																								
1653	Preparation of Project Description	126 days	Mon 9/7/15	Fri 2/26/16	Mon 9/7/15	Fri 2/26/16																								

Project: PG&E Topock Remediation Project  
 Date: Fri 5/11/18  
 Page 2 of 4

Tasks Not Started/In Progress		Overall Task Duration		Manual Task		Start-only	
Tasks Finished		Inactive Task		Duration-only		Finish-only	
Baseline Schedule		Inactive Milestone		Manual Summary Rollup			
Milestone		Inactive Summary		Manual Summary			

edays = calendar days; days = work days  
 Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).  
 \*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:  
 PG&E Federal Agencies CWG/TWG Public  
 DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions  
 - Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.  
 - Actual dates may vary depending on field conditions.

# HANDOUT 9A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 38) MAY 16, 2018 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2018				2019				2020				2021				2022				2023			
							Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
1654	Prepare Admin Draft SEIR	72 days	Fri 4/1/16	Mon 7/11/16	Fri 4/1/16	Mon 7/11/16																								
1655	2nd Admin Draft SEIR	17.8 wks	Fri 6/24/16	Wed 10/26/16	Fri 6/24/16	Wed 10/26/16																								
1656	Screencheck Draft SEIR	56 days	Thu 10/27/16	Thu 1/12/17	Thu 10/27/16	Thu 1/12/17																								
1657	ESA Prepare Screencheck SEIR	3 wks	Thu 10/27/16	Wed 11/16/16	Thu 10/27/16	Wed 11/16/16																								
1658	DTSC Review Screencheck SEIR	2.4 wks	Thu 11/17/16	Fri 12/2/16	Thu 11/17/16	Fri 12/2/16																								
1659	ESA Address DTSC Comments on Screencheck SEIR	2 wks	Mon 12/5/16	Fri 12/16/16	Mon 12/5/16	Fri 12/16/16																								
1660	ESA Finalize/Print/Distribute Draft SEIR	3.8 wks	Mon 12/19/16	Thu 1/12/17	Mon 12/19/16	Thu 1/12/17																								
1661	Draft SEIR Public Review	33 days	Thu 1/12/17	Mon 2/27/17	Thu 1/12/17	Mon 2/27/17																								
1662	45-day Public Review	46.38 edays	Thu 1/12/17	Mon 2/27/17	Thu 1/12/17	Mon 2/27/17																								
1663	Public Meetings	2 days	Thu 1/31/17	Wed 2/1/17	Tue 1/31/17	Wed 2/1/17																								
1664	Final EIR, Response to Comments (RTCs), Findings, MMRP	295 days	Tue 3/7/17	Tue 4/24/18	Tue 3/7/17	Tue 4/24/18																								
1665	Draft SEIR Comment Review and Categorization	3.8 wks	Tue 3/7/17	Fri 3/31/17	Tue 3/7/17	Fri 3/31/17																								
1666	ESA Prepare 1st Admin Draft Final SEIR	8 wks	Mon 4/3/17	Fri 5/26/17	Mon 4/3/17	Fri 5/26/17																								
1667	DTSC Review 1st Admin Draft Final SEIR	5 wks	Mon 5/29/17	Fri 6/30/17	Mon 5/29/17	Fri 6/30/17																								
1668	ESA Prepare 2nd Admin Draft Final SEIR	3 wks	Mon 7/3/17	Fri 7/21/17	Mon 7/3/17	Fri 7/21/17																								
1669	DTSC Review 2nd Admin Draft SEIR	2 wks	Mon 7/24/17	Fri 8/4/17	Mon 7/24/17	Fri 8/4/17																								
1670	ESA Prepare Screencheck Final SEIR/Findings	3 wks	Mon 8/7/17	Fri 8/25/17	Mon 8/7/17	Fri 8/25/17																								
1671	DTSC Review Screencheck Final SEIR/Findings	14.2 wks	Mon 8/28/17	Mon 12/4/17	Mon 8/28/17	Mon 12/4/17																								
1672	ESA Prepare Final SEIR for 30-day Circulation	2.6 wks	Tue 12/5/17	Thu 12/21/17	Tue 12/5/17	Thu 12/21/17																								
1673	30 Day Final SEIR Circulation	32.38 edays	Thu 12/21/17	Mon 1/22/18	Thu 12/21/17	Mon 1/22/18																								
1674	DTSC Certifies Final SEIR/ESA Files NOD	0 days	Tue 4/24/18	Tue 4/24/18	Tue 4/24/18	Tue 4/24/18																								
1675	DTSC reviews/approves Final Design and Construction/Remedial Action Work Plan	635 days	Thu 11/19/15	Tue 4/24/18	Thu 11/19/15	Tue 4/24/18																								
1676	DOI reviews/approves Final Design and Construction/Remedial Action Work Plan	620 days	Thu 11/19/15	Tue 4/3/18	Thu 11/19/15	Tue 4/3/18																								
1677	Community Outreach	1710 days	Fri 10/7/11	Tue 4/24/18	Fri 10/7/11	Tue 4/24/18																								
1687	Project Contracting	2.9 mons	Wed 4/4/18	Wed 6/27/18	Wed 4/4/18	NA																								
1688	Construction (this is a preliminary construction schedule for planning purposes)	1369.6 days	Wed 6/27/18	Mon 9/25/23	NA	NA																								
1689	Pre-Construction	67 days	Wed 6/27/18	Sun 9/30/18	NA	NA																								
1690	Stakeholder Attending Mobilization Kick-Off Meeting at Site	0 days	Wed 6/27/18	Wed 6/27/18	NA	NA																								
1691	Stakeholder Attending Mobilization Kick-Off Meeting at Site	0 days	Wed 6/27/18	Wed 6/27/18	NA	NA																								
1692	Stakeholder Attending Mobilization Kick-Off Meeting at Site	0 days	Wed 6/27/18	Wed 6/27/18	NA	NA																								
1693	Stakeholder Attending Mobilization Kick-Off Meeting at Site	0 days	Wed 6/27/18	Wed 6/27/18	NA	NA																								
1694	Stakeholder Attending Mobilization Kick-Off Meeting at Site	0 days	Wed 6/27/18	Wed 6/27/18	NA	NA																								
1695	Mobilization (Setup temp construction trailers, construction water, construction signage, access routes, etc.)	95 edays	Wed 6/27/18	Sun 9/30/18	NA	NA																								
1696	Construction and Start-up Activities	1301.6 days	Tue 10/2/18	Mon 9/25/23	NA	NA																								
1697	Stakeholder Attending Construction Kick-Off Meeting at Site	0 days	Tue 10/2/18	Tue 10/2/18	NA	NA																								
1698	Stakeholder Attending Construction Kick-Off Meeting at Site	0 days	Tue 10/2/18	Tue 10/2/18	NA	NA																								
1699	Stakeholder Attending Construction Kick-Off Meeting at Site	0 days	Tue 10/2/18	Tue 10/2/18	NA	NA																								
1700	Stakeholder Attending Construction Kick-Off Meeting at Site	0 days	Tue 10/2/18	Tue 10/2/18	NA	NA																								
1701	Stakeholder Attending Construction Kick-Off Meeting at Site	0 days	Tue 10/2/18	Tue 10/2/18	NA	NA																								
1702	Major Phase 1 Construction Activities	510 days	Wed 10/3/18	Tue 9/15/20	NA	NA																								
1703	Build Construction Headquarters	6.75 mons	Wed 10/3/18	Wed 4/17/19	NA	NA																								
1704	Build Soil Processing Yard	2.6 mons	Mon 11/12/18	Thu 1/24/19	NA	NA																								
1705	Install Remedy Storm Drain at Transwestern Bench	23 edays	Tue 2/5/19	Thu 2/28/19	NA	NA																								

Project: PG&E Topock Remediation Project  
Date: Fri 5/11/18  
Page 3 of 4

**Tasks Not Started/In Progress** [Hatched pattern]    **Overall Task Duration** [Black arrow]    **Manual Task** [Thick black bar]    **Start-only** [Light blue bar]

**Tasks Finished** [Solid blue bar]    **Inactive Task** [White bar]    **Duration-only** [Thin grey bar]    **Finish-only** [Dark blue bar]

**Baseline Schedule** [Dotted pattern]    **Inactive Milestone** [Diamond]    **Manual Summary Rollup** [Thick blue bar]

**Milestone** [Blue diamond]    **Inactive Summary** [White arrow]    **Manual Summary** [Thin black bar]


edays = calendar days; days = work days  
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).  
\*Timeframes shown are for planning purpose. Actual timeframes may vary.

**Color Coding:**  
PG&E Federal Agencies CWG/TWG Public  
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

**Major Assumptions**  
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.  
- Actual dates may vary depending on field conditions.

## HANDOUT 9A - TOPOCK REMEDIATION PROJECT SCHEDULE (REV. 38) MAY 16, 2018 CWG MEETING

ID	Task Name	Duration	Forecasted Start	Forecasted Finish	Actual Start	Actual Finish	2018		2019				2020				2021				2022				2023				
							Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3
1706	Install Pilot Borings, Monitoring Wells, and Remediation Wells	19 mons	Thu 11/1/18	Mon 5/11/20	NA	NA																							
1707	Build IRZ Ring Road	28 edays	Wed 4/17/19	Wed 5/15/19	NA	NA																							
1708	Install Remedy Pipelines	5.5 mons	Mon 2/4/19	Mon 7/15/19	NA	NA																							
1709	Install Remedy Facilities at MW-20 Bench	6 mons	Mon 5/13/19	Mon 11/4/19	NA	NA																							
1710	Install Remedy Facilities at TCS and TCS Ponds	11.1 mons	Tue 6/4/19	Fri 4/24/20	NA	NA																							
1711	Install Electrical and Control System	17 mons	Wed 1/30/19	Thu 6/11/20	NA	NA																							
1712	Site Stabilization/Revegetation	20 mons	Fri 11/23/18	Wed 7/1/20	NA	NA																							
1713	System Integration and Functional Testing	99 edays	Mon 6/8/20	Tue 9/15/20	NA	NA																							
1714	Shut down IM and Start-up IRZ	12.5 mons	Wed 9/16/20	Thu 9/16/21	NA	NA																							
1715	Construct Phase 2 Components Construction (Freshwater Injection System, Inner Recirculation Loop, and TCS Recirculation Loop, Wells)	12.5 mons	Thu 9/16/21	Mon 9/19/22	NA	NA																							
1716	Commissioning and Start-up Freshwater Injection	6 mons	Tue 9/20/22	Tue 3/14/23	NA	NA																							
1717	Start-up Inner Recirculation/TCS Loop	6 mons	Wed 3/15/23	Wed 9/6/23	NA	NA																							
1718	Start-up Complete/Start Full Remedy Operations	0 days	Thu 9/7/23	Thu 9/7/23	NA	NA																							
1719	Construction Close-out	12.6 mons	Tue 9/20/22	Mon 9/25/23	NA	NA																							
1720	<b>Reporting</b>	<b>905 days</b>	<b>Mon 11/19/18</b>	<b>Wed 5/4/22</b>	<b>NA</b>	<b>NA</b>																							
1721	Prepare/submit monthly construction progress reports	43.1 mons	Mon 11/19/18	Wed 5/4/22	NA	NA																							
1722	Start Operation and Maintenance	0 days	Fri 9/8/23	Fri 9/8/23	NA	NA																							

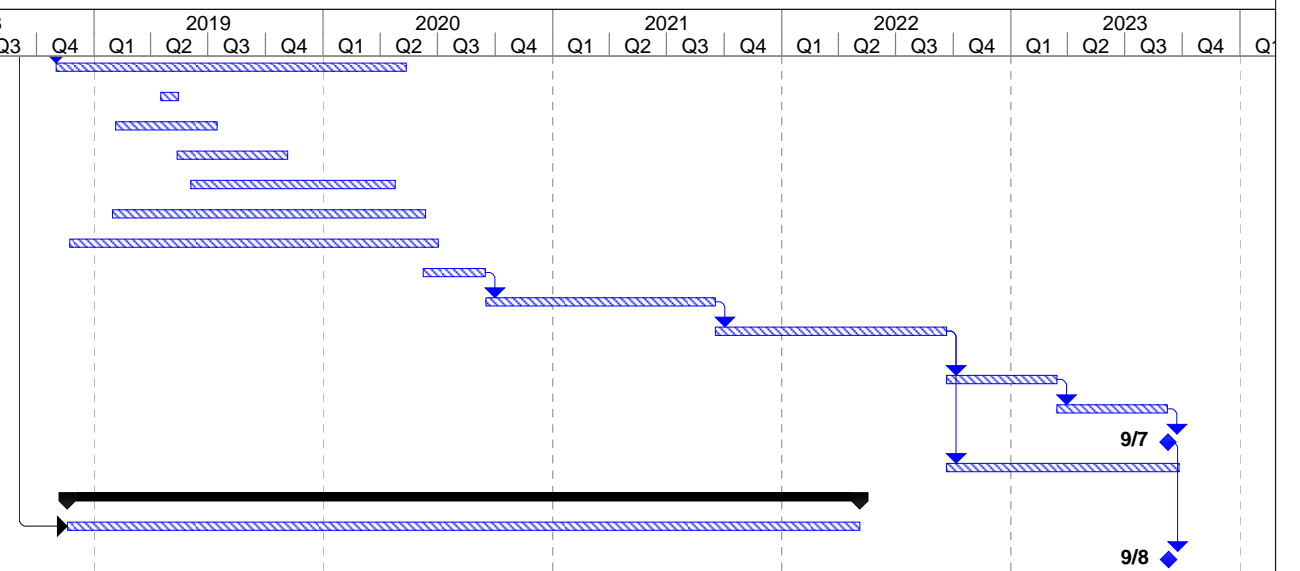

Project: PG&E Topock Remediation Project  
Date: Fri 5/11/18  
Page 4 of 4

Tasks Not Started/In Progress		Overall Task Duration		Manual Task		Start-only	
Tasks Finished		Inactive Task		Duration-only		Finish-only	
Baseline Schedule		Inactive Milestone		Manual Summary Rollup			
Milestone		Inactive Summary		Manual Summary			

edays = calendar days; days = work days  
Baseline Schedule is the 8/15/07 CWG Schedule (rev 1, 12/12/07).  
\*Timeframes shown are for planning purpose. Actual timeframes may vary.

Color Coding:  
PG&E Federal Agencies CWG/TWG Public  
DTSC Tribes/SHPO Other CA Agencies AZ Agencies

Major Assumptions  
- Permits, CWG/ stakeholder review, and DTSC review & approvals are estimated.  
- Actual dates may vary depending on field conditions.
